




AWDS Timeline of Change: instructed change and AtkinsRéalis delivery, by package

● Change instructed ◆ Delivered by AtkinsRéalis ○ Descoped

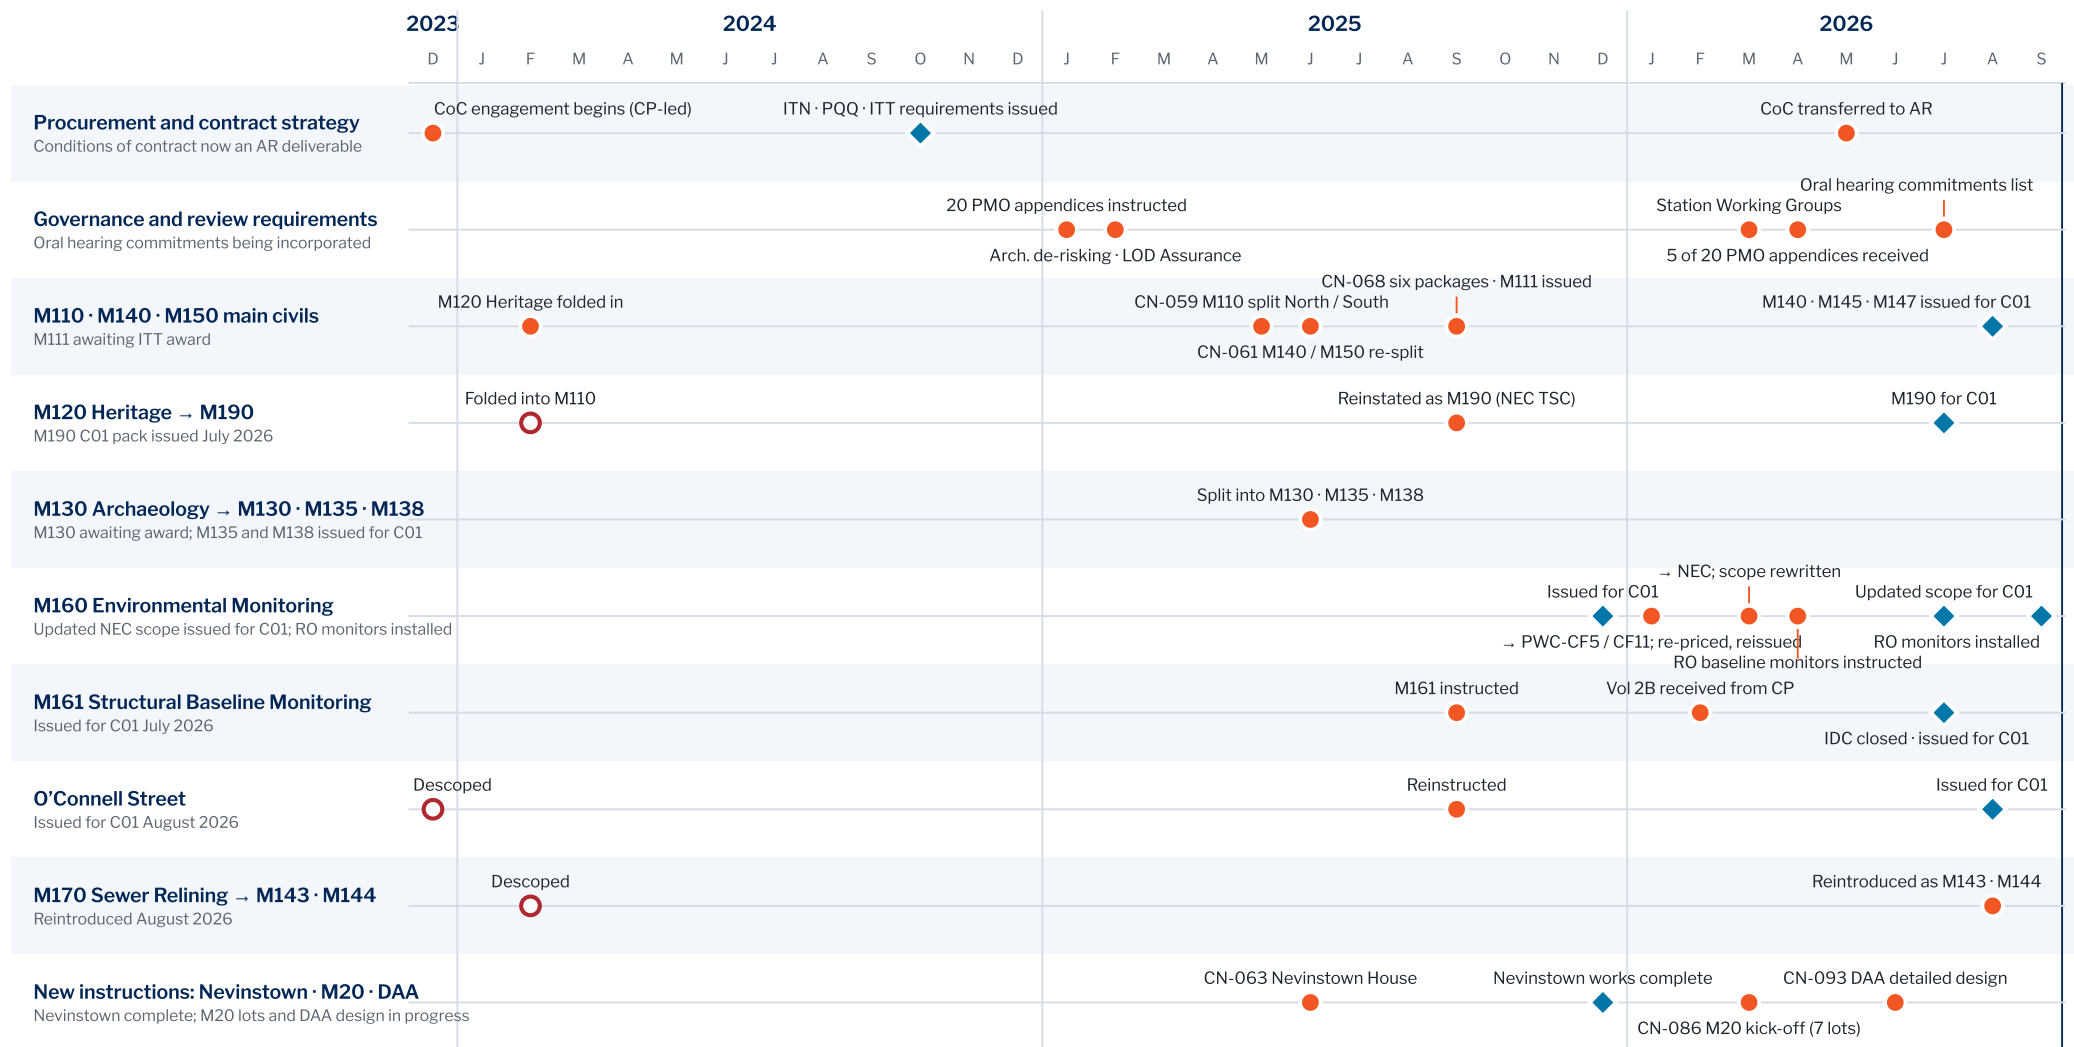

Report date 15 September 2026

35 dated events: 23 changes instructed, 9 items delivered, 3 descoped. Dates are at month level, as recorded in the AWDS Timeline of Change record, 15 September 2026. Items without a recorded month (CN-031 draft CEMPs, M135 and M138 C01 issue, market engagement, Stage Gate 5A) are listed in Appendix C.

**Headline KPI: Adaptability and Delivery**

Definition. The team's capacity to absorb instructed change without loss of output. Measured by instructions actioned against scope packs issued for acceptance and works completed in the same period.

Evidence to 15 September 2026.


- 7 formal change notices and a further 17 dated instructions and notifications actioned (Appendix B).
- Package count from 7 to 25; three restructurings of the main civils packages between May and September 2025.
- 9 scope packs issued for C01 acceptance; 2 physical works packages completed.
- M160 issued for C01 under each of three contract forms in seven months.
- Descoped items returned and delivered: O'Connell Street, Heritage (M120 to M190), Sewer relining (M170 to M143 and M144).

Scope absorbed beyond the Conditions of Engagement

- Conditions of contract for all packages (May 2026)
- Master construction programme (undated)
- Market engagement: 2023 lead; 2025 interviews and roadshow (2023, 2025)
- Stage Gate 5A: Detailed Design Report, baseline estimates, conditions of contract strategy (undated)
- Railway Order baseline monitoring: procure, install, manage (April 2026)
- Interface leadership: BusConnects, DAA (undated)

Output in development at report date

- M111 (TBM portal) designed and procured; awaiting ITT award.
- M130 awaiting contract award.
- M20 Minor Works: 7 lots being scoped and designed (CN-086).
- Dublin Airport advance works detailed design (CN-093).
- More than 100 draft CEMPs (CN-031).

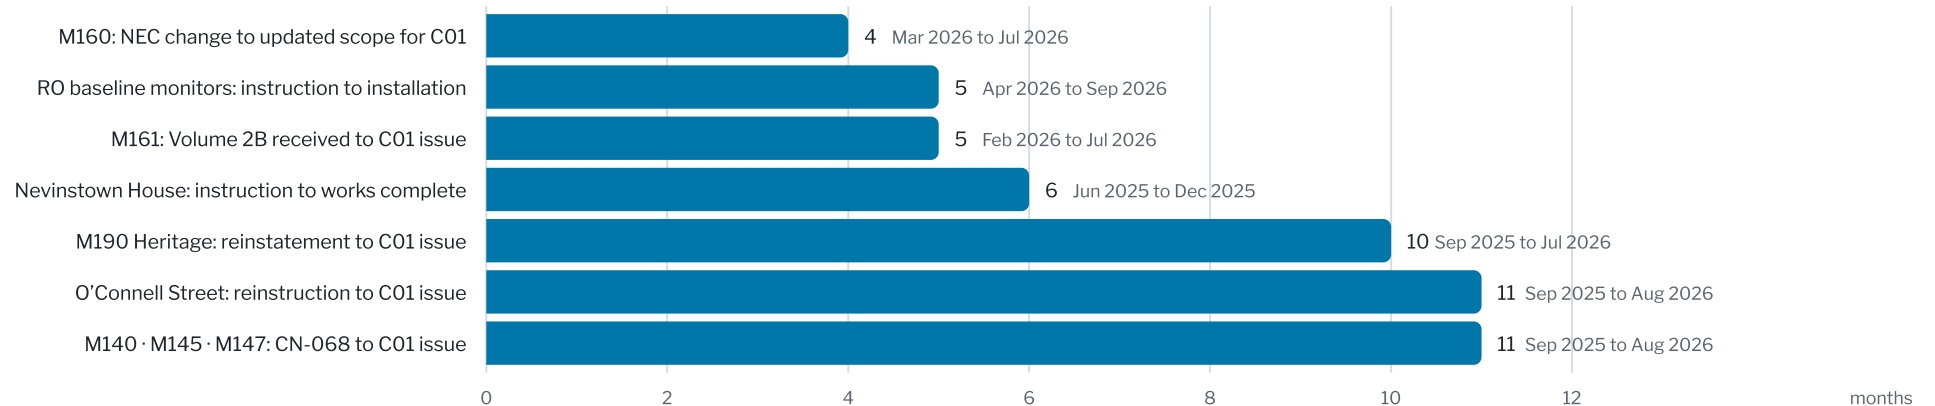Responsiveness: instruction to issue or completion

Elapsed months between the month-level dates recorded in the source. Bars are ordered shortest to longest.



KPI framework for the AWDS team

Five measures, led by Adaptability and Delivery. Each is defined so that it can be reported from the change register and the document issue record without additional data collection. Evidence to date is drawn from Appendices B and C; the proposed measure is the definition for quarterly reporting going forward.

KPI	What it measures	Evidence to 15 September 2026	Proposed reporting measure
1. Adaptability and Delivery	Instructed change absorbed without loss of output.	7 change notices actioned; 9 packs issued for C01; 2 works delivered; package count 7 to 25.	Per quarter: instructions received, instructions closed, packs issued for C01, packs accepted.
2. Responsiveness	Elapsed time from instruction to issue or completion.	4 to 11 months across the seven measured items (chart above).	Months from instruction to C01 issue, per package; months from instruction to completion, per works item.
3. Scope absorption	Responsibilities taken on beyond the CoE scope.	6 responsibilities transferred from the CP (listed above).	Register of absorbed responsibilities: item, instructing party, date, resource effect.
4. Quality at issue	Reviews closed before a pack is issued for acceptance.	M160 issued after peer review close-out (Dec 2025). M161 IDC held and all comments incorporated before issue (Jul 2026).	Share of packs issued with IDC and peer review comments closed; review rounds per pack.
5. Interface leadership	Interfaces and engagements led by the team on the client's behalf.	BusConnects and DAA interfaces led by AR staff; market engagement led in 2023; 2025 interviews and first MetroLink roadshow supported.	Interfaces led; engagements delivered; actions closed.

Reading the headline measure

Adaptability and Delivery is reported as a pair: the count of instructions closed in the period, and the count of packs issued for acceptance or works completed in the same period. Read together they show whether output was sustained while the package structure changed. The register in Appendix B is the audit trail for both counts.



Package evolution: original seven to current 25

Original contract packages (7)

Package	What happened to it
M110	Split North/South (CN-059, May 2025); recombined with M140 and M150 and re-split into six packages (CN-068, Sep 2025)
M120	Heritage folded into M110 (Feb 2024); reinstated as M190 under NEC TSC (Sep 2025)
M130	Archaeology split into M130, M135 and M138 (Jun 2025)
M140	Geographical split altered (CN-061, Jun 2025); recombined and re-split under CN-068 (Sep 2025)
M150	Geographical split altered (CN-061, Jun 2025); recombined and re-split under CN-068 (Sep 2025)
M160	Environmental Monitoring; contract form changed twice (Jan and Mar 2026); M161 added (Sep 2025)
M170	Sewer Relining descope (Feb 2024); reintroduced as M143 and M144 (Aug 2026)

Current contract packages (25)

Group	Packages	No.
From M110, M140 and M150 (CN-068 six)	M140, M141, M142, M145, M146, M147	6
TBM portal (outside the CN-068 six)	M111	1
From M130 Archaeology	M130, M135, M138	3
Environmental and structural monitoring	M160, M161	2
Heritage (formerly M120)	M190	1
Sewer relining (formerly M170)	M143, M144	2
M20 Minor Works	M20 lot 1, M20 lot 2, M20 lot 3, M20 lot 4, M20 lot 5, M20 lot 6, M20 lot 7	7
Instructed works and services	Nevinstown House demolition, DAA design works, Environmental baseline monitoring	3
Total		25

M20 Minor Works is counted as its seven lots. M143 and M144 (sewer relining, reintroduced August 2026) are included. M111 sits outside the six packages created under CN-068.



Change register: dated events, December 2023 to September 2026

Date	Reference	Package / area	Type	Event	AtkinsRéalis response and status
Dec 2023	Instruction	O'Connell Street	● Descoped	Descoped.	Removed from AR workload.
Dec 2023	None	Conditions of contract	● Change instructed	Engagement on the conditions of contract for the packages began, led by the Client Partner (CP).	AR contributed to CP-led drafting.
Feb 2024	Instruction	M110	● Change instructed	M120 Heritage instructed to be included within the M110 contract.	M110 scope extended.
Feb 2024	Instruction	M120 Heritage	● Descoped	Heritage instructed to be included within the M110 contract; no longer a standalone package.	Scope carried within M110.
Feb 2024	Instruction	M170 Sewer Relining	● Descoped	Descoped.	Removed from AR workload.
Oct 2024	None	Procurement	● Delivered by AtkinsRéalis	Henry Corcoran developed the ITN, PQQ and associated ITT requirements and issued them to the CP. The ERO was delayed and the documents were held.	Following the ERO the contracting strategy changed, the package count almost tripled and LOD requirements added materially to the work carried by the team.
Jan 2025	Instruction	PMO Project Controls appendices	● Change instructed	Instruction to include 20 Project Controls appendices, to be produced by the PMO team, in the scope documents prior to ITT.	5 of the 20 appendices were issued to AR in April 2026; AR reviews and incorporates each on receipt.
Feb 2025	Instruction	Programme-wide	● Change instructed	Archaeological de-risking instructed. LOD Assurance and its associated work first introduced to AR.	Both absorbed into the design and documentation workload.
May 2025	CN-059	M110	● Change instructed	Instruction to split M110 into two contracts, North and South.	Package documentation restructured.
Jun 2025	CN-061	M140, M150	● Change instructed	Instruction to alter the geographical split of the M140 and M150 contracts.	Package boundaries and documentation revised.
Jun 2025	Instruction	M130 Archaeology	● Change instructed	M130 split into three contracts: M130, M135 and M138.	M130 now awaiting contract award. M135 and M138 issued for C01 approval (month not recorded).
Jun 2025	CN-063	Nevinstown House demolition	● Change instructed	Requirement for design, ITT pack and site supervision services for Nevinstown House.	Works designed, procured, supervised and completed by December 2025.
Sep 2025	CN-068	M110, M140, M150	● Change instructed	New contracting strategy: M110, M140 and M150 combined and split again into six geographically aligned packages (M140, M141, M142, M145, M146, M147). M111, a new package forming a key component of the TBM portal, issued to AR for design and procurement in the same month.	Six packages re-documented. M111 designed and procured by AR; awaiting ITT award.
Sep 2025	Instruction	M190 Heritage	● Change instructed	Heritage reintroduced as its own contract, M190, and changed from GCC to an NEC Term Service Contract.	New package documentation prepared under the NEC form.

Date	Reference	Package / area	Type	Event	AtkinsRéalis response and status
Sep 2025	Instruction	M161	● Change instructed	M161 Structural Baseline Monitoring works instructed.	Package opened; Volume 2B (Specification) to be developed by the CP.
Sep 2025	Instruction	O'Connell Street	● Change instructed	Reinstructed.	Design and documentation restarted.
Dec 2025	None	M160	● Delivered by AtkinsRéalis	Issued for C01 acceptance following peer review and comment close-out.	First issue under the original contract form.
Dec 2025	None	Nevinstown House demolition	● Delivered by AtkinsRéalis	Demolition works completed.	Six months from instruction to completion.
Jan 2026	Notification	M160	● Change instructed	Contract form changed to PWC-CF5 and PWC-CF11.	New pricing documents prepared for both forms, scope pack updated and reissued within the month.
Feb 2026	None	M161	● Change instructed	Volume 2B (Specification), developed by the CP, issued to AR.	AR developed the remaining scope documents, including cost and pricing documents, on receipt.
Mar 2026	None	Station Working Groups	● Change instructed	Station Working Groups established. Change requirements issued by the M400 team as a result.	AWDS designs updated to reflect revised station box layouts.
Mar 2026	Notification	M160	● Change instructed	Contract form changed again, to NEC. Scope documents required to reflect the new approach.	Scope documents rewritten for NEC.
Mar 2026	CN-086	M20 Minor Works	● Change instructed	M20 Minor Works kick-off meeting. Seven lots now being developed, scoped and designed where required by AR.	Seven contracts in development.
Apr 2026	None	PMO Project Controls appendices	● Change instructed	5 of the 20 PMO appendices instructed in January 2025 were issued to AR.	Reviewed and incorporated into the scope documents.
Apr 2026	Instruction	Railway Order baseline monitoring	● Change instructed	The M160 contractor would not be appointed in time for MetroLink to meet its Railway Order obligations on baseline monitoring. AR instructed to procure, manage and install the monitors required.	Monitors procured, installed and managed by AR; installation completed September 2026.
May 2026	Instruction	Conditions of contract	● Change instructed	The CP Commercial Lead left the project with the conditions of contract incomplete for every package.	AR instructed to take over completion of the conditions of contract for all packages ahead of ITT.
Jun 2026	CN-093	Dublin Airport advance works	● Change instructed	Instruction to undertake the detailed design for Dublin Airport advance works.	Detailed design in progress.
Jul 2026	None	Oral hearing commitments	● Change instructed	Final list of oral hearing commitments issued to AR.	Documentation and ITT packs updated to carry the commitments.
Jul 2026	None	M190 Heritage	● Delivered by AtkinsRéalis	M190 C01 pack issued for acceptance.	Ten months from reinstatement to issue.
Jul 2026	None	M160	● Delivered by AtkinsRéalis	Updated NEC scope issued for C01 approval.	Third contract form in seven months, issued.

Date	Reference	Package / area	Type	Event	AtkinsRéalis response and status
Jul 2026	None	M161	● Delivered by AtkinsRéalis	IDC held, all comments incorporated, issued for C01 approval.	Five months from receipt of Volume 2B to issue.
Aug 2026	None	M140, M145, M147	● Delivered by AtkinsRéalis	Three of the six packages issued for C01 acceptance.	Issued eleven months after CN-068.
Aug 2026	GC393/4	M143, M144	● Change instructed	Sewer relining reintroduced as two packages, M143 and M144, in GC393/4.	Two new packages opened.
Aug 2026	None	O'Connell Street	● Delivered by AtkinsRéalis	Issued for C01 approval.	Eleven months from reinstruction to issue.
Sep 2026	None	Railway Order baseline monitoring	● Delivered by AtkinsRéalis	Baseline monitors installed, satisfying the Railway Order requirement.	Five months from instruction to installation.

Dates are given to the month, as recorded in the source. Volume 2B for M161 was developed by the CP and issued to AtkinsRéalis in February 2026; the expected date stated in the source is not reproduced here pending confirmation.



Further items requiring the team to adapt approach and resources

Reference	Item	Change	AtkinsRéalis response
CN-031	Draft CEMPs	Instruction to develop draft Construction Environmental Management Plans for the contract packages where required.	More than 100 draft CEMP documents in development.
None	Market engagement (2023)	MetroLink was not set up for market engagement requirements in 2023.	Henry Corcoran led market engagement in lieu of the CP: preparing meetings, taking notes and reporting the engagement summary to the Client.
None	Market engagement (2025)	Market engagement interviews and the first MetroLink roadshow in Dublin.	The AR team led a significant share of the interviews at short notice and assisted the roadshow deployment.
None	Stage Gate 5A	The CP was intended to lead Stage Gate 5A.	AR produced the Detailed Design Report, the baseline estimates and the conditions of contract strategy.
None	Master construction programme	AR was scoped under the CoE to prepare one construction programme; the master construction programme was to be managed and developed by the CP.	The master construction programme is now an AR deliverable.
None	Interface leadership	Key interfaces including BusConnects and DAA required leads.	Several AR team members requested to lead these interfaces.
None	Contract strategy and framework approach	Contract strategies changed and methodology moved to a framework approach.	Documentation and procurement approach revised accordingly.
None	Document templates and numbering	Several changes to document templates and to document numbering.	Re-templating and renumbering of issued and in-progress documents.
None	Schedule Optimisation	Schedule Optimisation introduced.	Incorporated into programme and package planning.
None	Station box layouts	Station box layouts changed, affecting AWDS designs.	AWDS designs updated for each change.
None	MetroLink policy documents	Policy documents still being updated and issued.	Scope documents kept aligned as policies are released.
None	Public consultation	Two additional rounds of public consultation.	Design and scope changes carried through the packages.
None	Functional review comments	A high proportion of functional review comments were assessed as not applicable to the documents reviewed; each still required a written response. Comment responses were frequently returned late, and positions taken by a team or department sometimes changed between rounds.	Every comment answered and closed; additional review rounds absorbed.
None	Client ProjectWise (CDE)	The Scope of Services anticipated the project CDE would be available by the end of 2022 at the latest. It is not yet fully functional.	Information transfer between AR and the CP has been slower than planned throughout; interim exchange routes used.

These items have no month recorded in the source and are therefore not plotted on the timeline.



Term	Meaning
AR	AtkinsRéalis
AWDS	Advance Works Design Services
C01	Document acceptance code; “issued for C01” means issued for client acceptance
CDE	Common Data Environment (ProjectWise)
CEMP	Construction Environmental Management Plan
CN	Change Notice
CoC	Conditions of Contract
CoE	Conditions of Engagement (Irish public sector consultancy agreement)
CP	Client Partner
DAA	Dublin Airport Authority
ERO	Enforceable Railway Order

Source and method

All content is drawn from the AWDS Timeline of Change record, 15 September 2026. Events with a recorded month are plotted on the timeline and listed in Appendix B; events without one are listed in Appendix C. Counts on the summary page are derived from those lists: the package count from Appendix A, change notices and C01 issues from Appendix B, and elapsed durations from the difference between month-level dates.

Term	Meaning
GCC	Irish public sector contract form under which M190 was first to be procured
IDC	Interdisciplinary design check
ITN / PQQ / ITT	Tender-stage documents: invitation to negotiate, pre-qualification questionnaire, invitation to tender
LOD	Level of Design
NEC TSC	NEC Term Service Contract
PMO	Project Management Office
PWC-CF5 / CF11	Public Works Contract forms CF5 and CF11 (Irish Capital Works Management Framework)
RO	Railway Order
TBM	Tunnel boring machine
M400	MetroLink M400 team, source of Station Working Group change requirements

Marker key

● Change instructed ◆ Delivered by AtkinsRéalis ○ Descoped

Colours follow the MetroLink palette. The three marker colours were checked for colour-vision separation and contrast; marker shape carries the same distinction for greyscale printing.
