


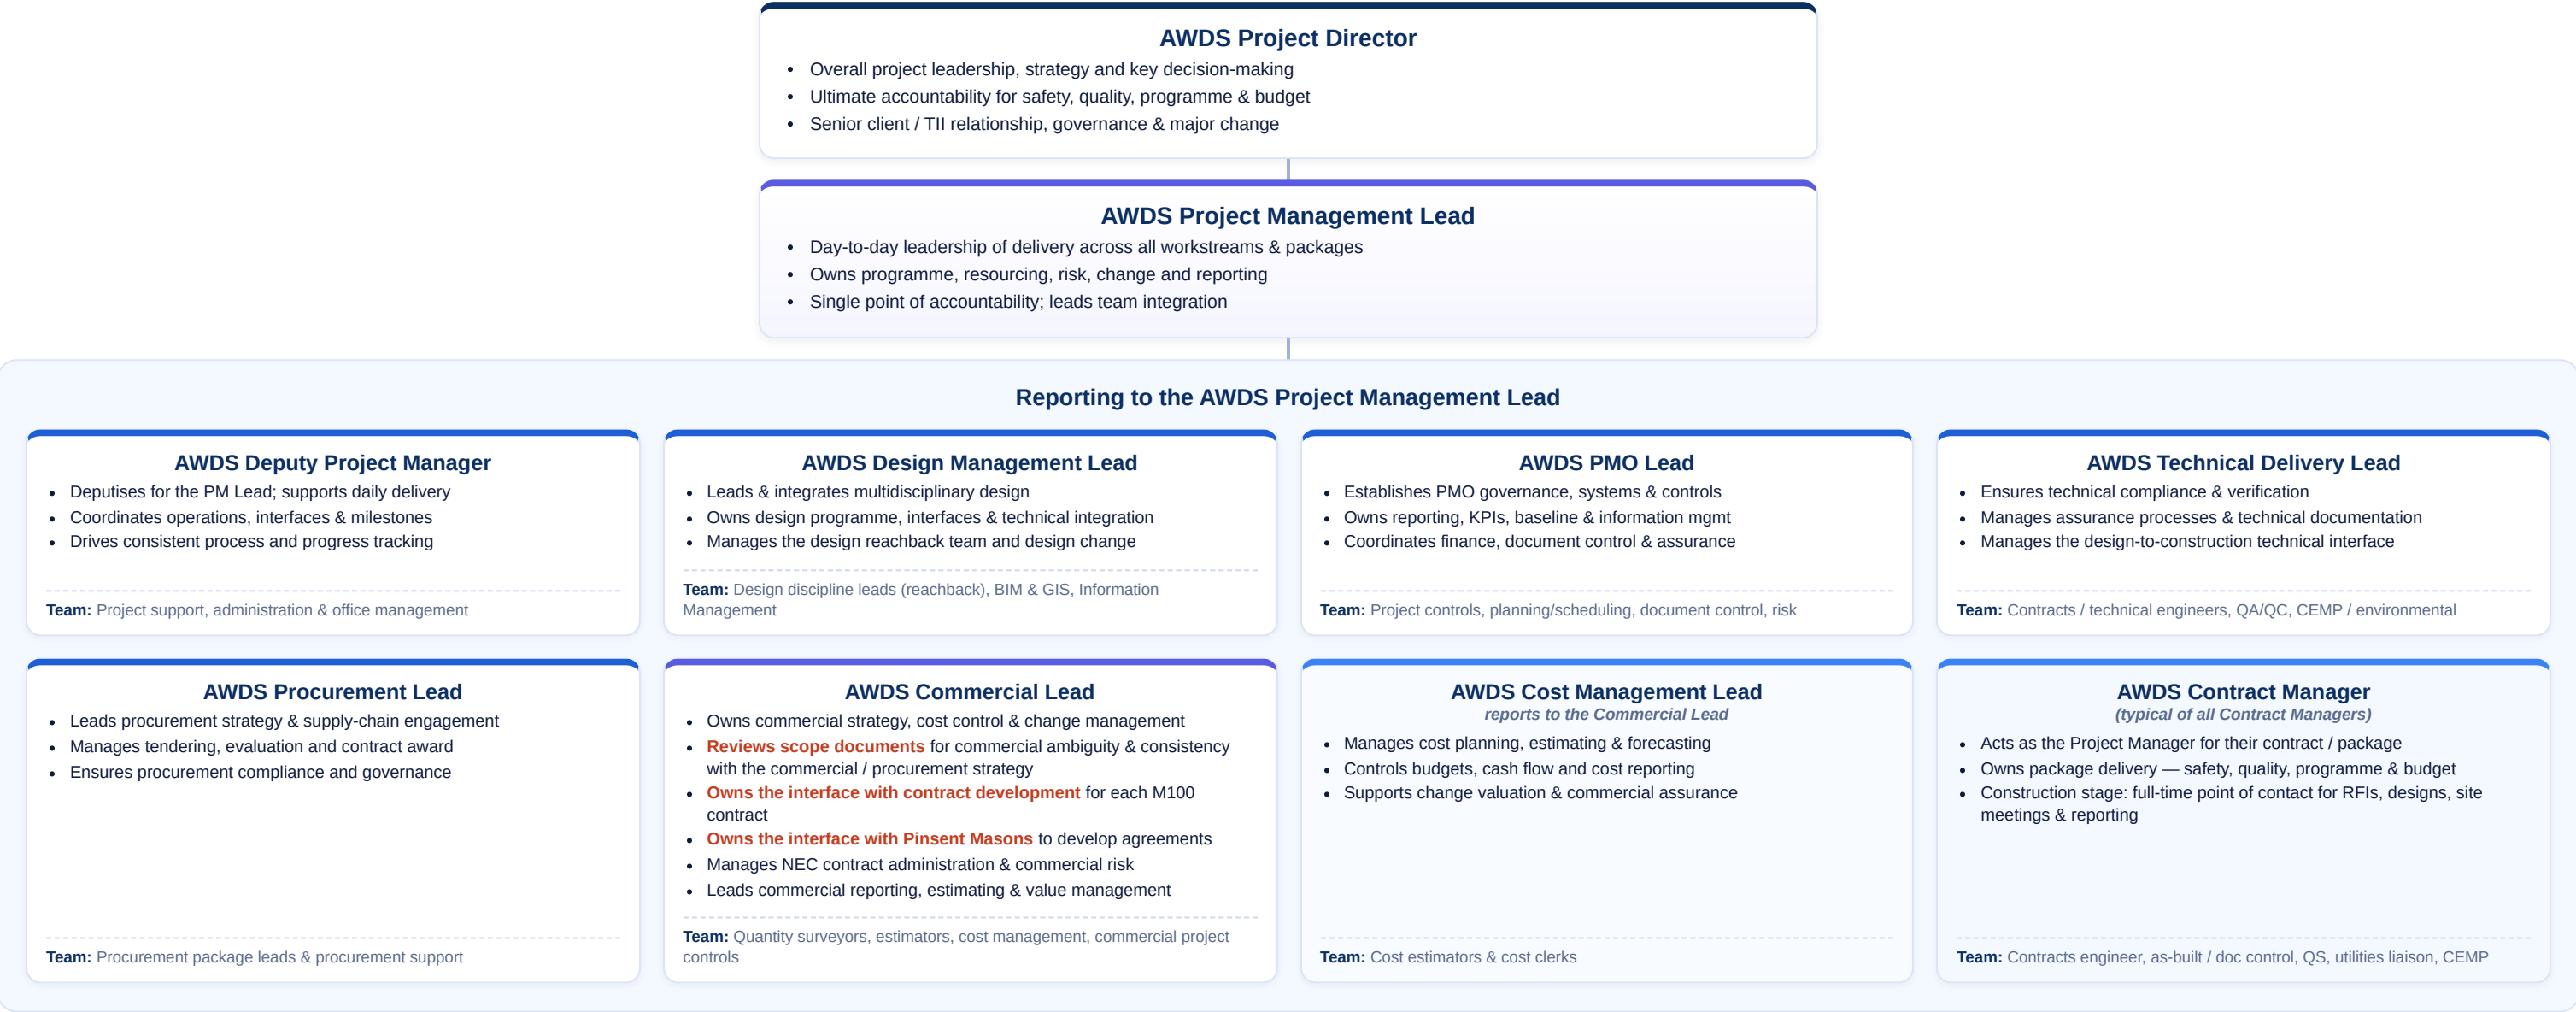

Package-lead ownership: Contract & Procurement Package Leads own their package meetings, action logs and monthly reporting — keeping the wider team joined up. Standard agendas and a common monthly report format are used across all contracts.

Standard meeting cadence (per contract)

Meeting	Frequency	Owner / Chair	Attendees	Purpose
Weekly Progress & Coordination	Weekly	Contract Manager	CM team + contractor PM	RFIs, day-to-day queries, 2-week look-ahead, site coordination
Design & Technical Review	Fortnightly	Contract Manager + Design Management Lead	Design (reachback) leads, contractor design team	Review contractor design proposals, technical queries, as-built status
Commercial / NEC Review	Monthly	Commercial Lead (+ package QS)	CM, QS, Cost Management	Compensation events / change, applications, forecast, commercial risk
Procurement & Package Coordination	Monthly	Procurement Package Lead	Procurement, Contract Manager	Package procurement status, interfaces, joined-up forward planning
Utility Asset Owner Liaison	Monthly / as required	Utilities Liaison + Contract Manager	Utility asset owners	Approvals, dependencies and coordination with asset owners
Monthly Contract Review	Monthly	Contract Manager	Commercial, Technical, Design, Procurement reps	Consolidated progress, risk, change, programme & reporting for the package
Programme Integration Board	Monthly	AWDS Project Management Lead	All Contract & Procurement Package Leads	Cross-package alignment, dependencies, escalation & joined-up delivery

Monthly rhythm

Week 1

- Weekly progress & coordination
- Design & technical review
- RFI & design-proposal status

Week 2

- Commercial / NEC review
- Procurement & package coordination
- Change & risk updates

Week 3

- Utility asset-owner liaison
- As-built drawing updates
- Forecast & programme refresh

Week 4

- Monthly contract review
- Package monthly report issued
- Feeds the Programme Integration Board
